



Rio Neighborhood Sidewalks

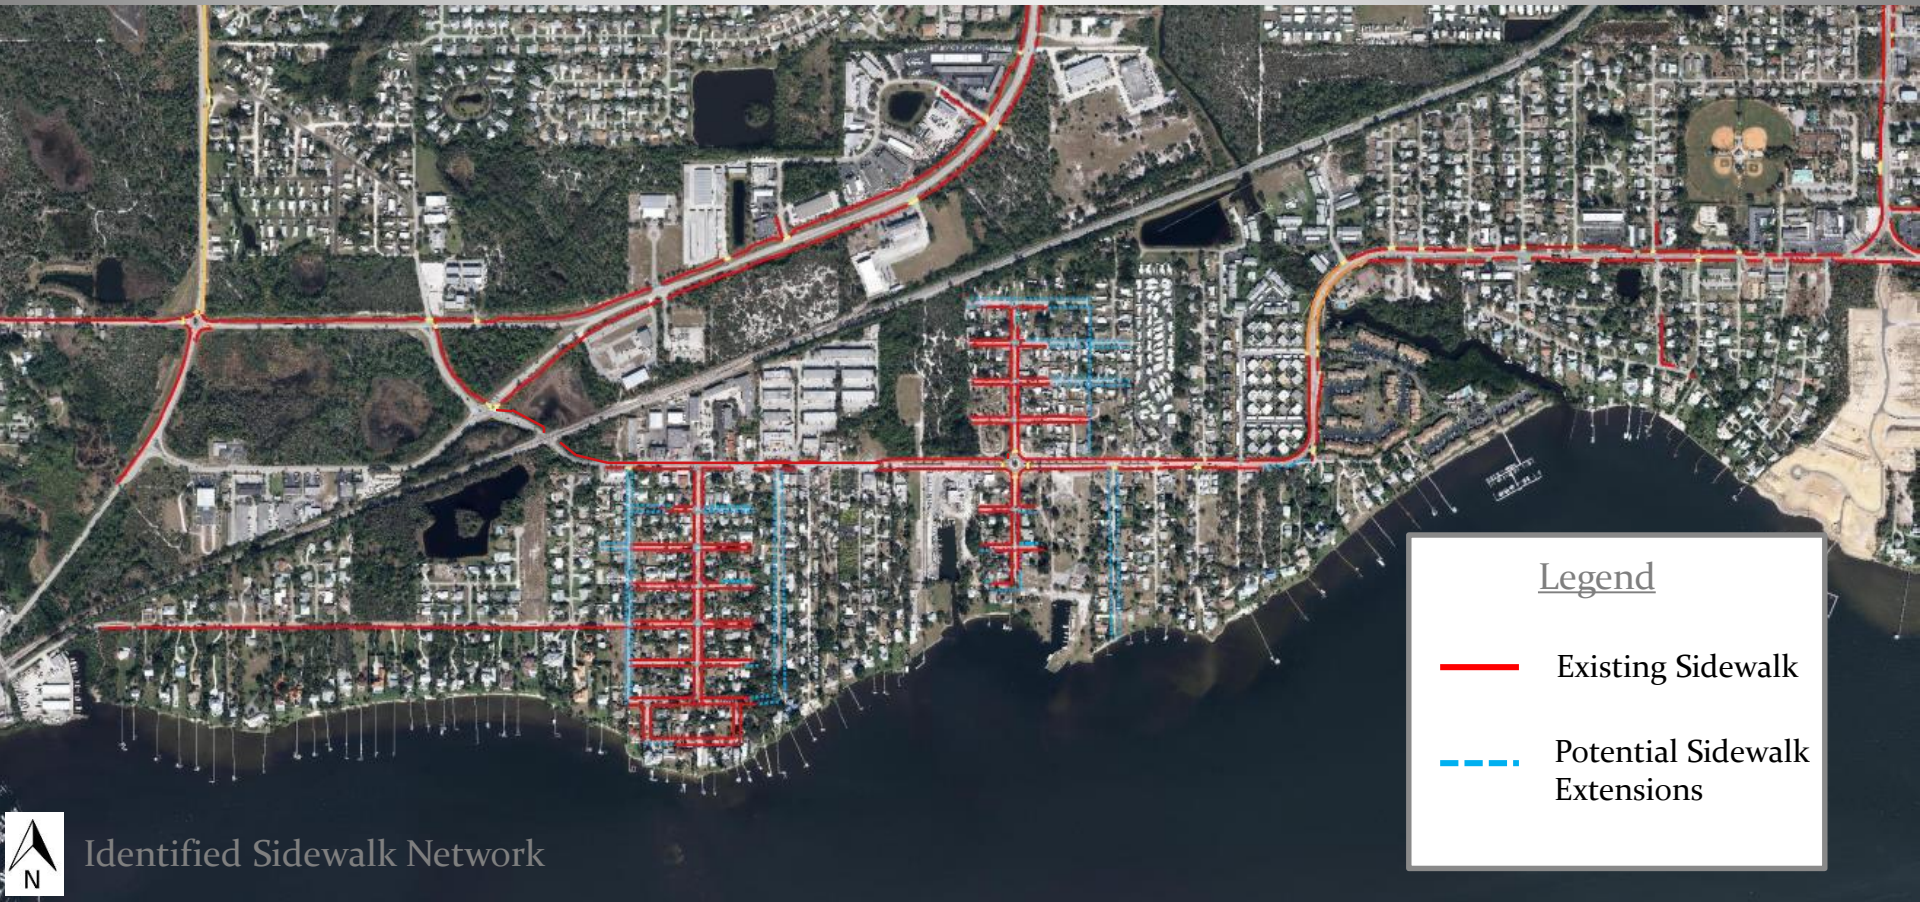

NAC FOCUS AREA

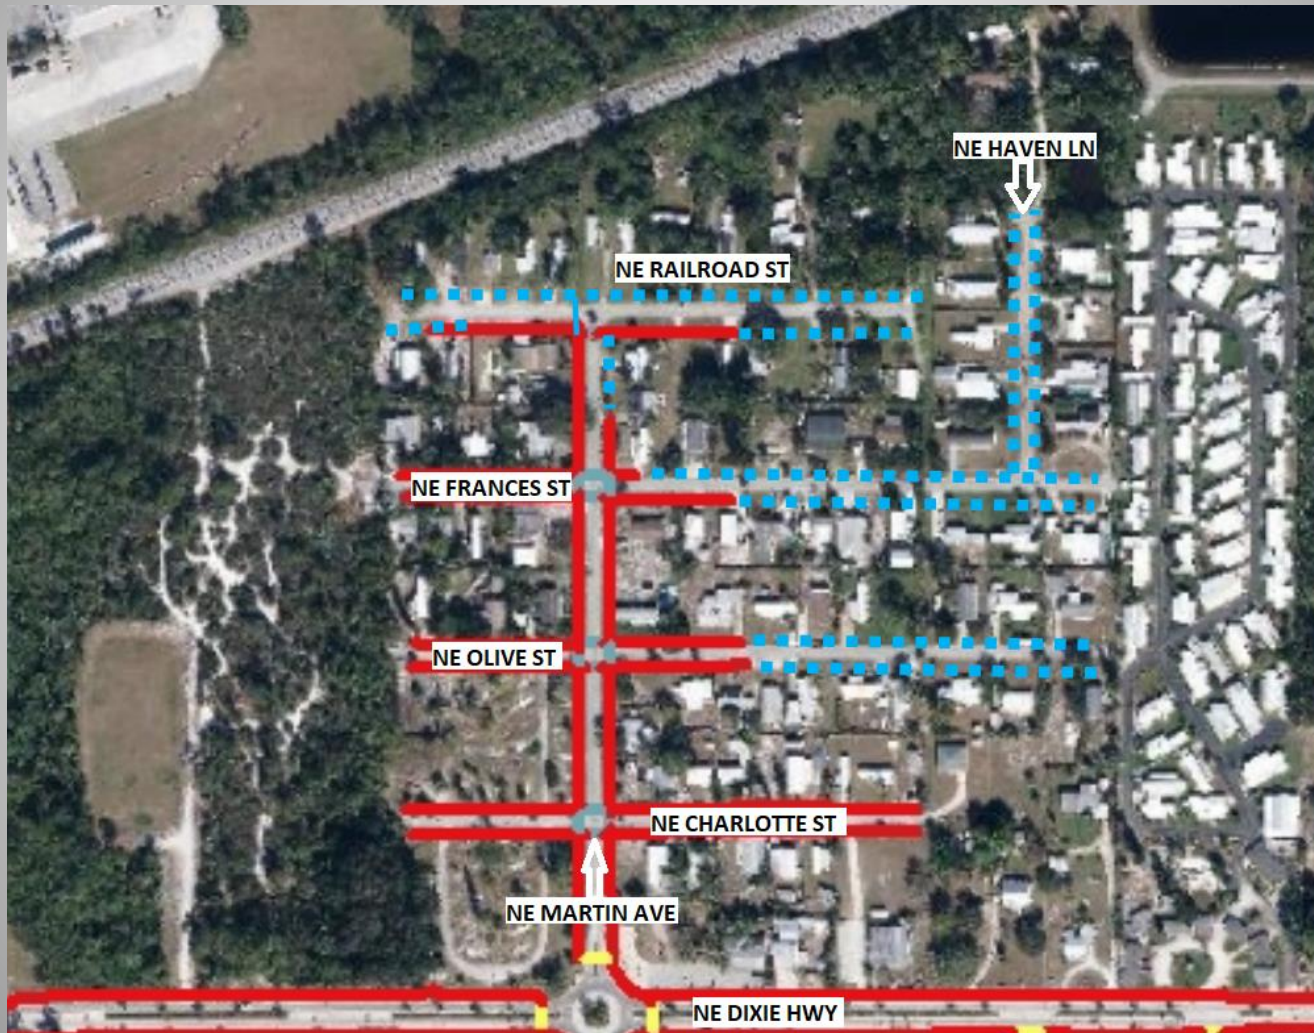

Completed Project

Rio: Sidewalk Installation



Broken Sidewalk
Replaced with 6'
Sidewalk

*498 Feet

New 6' Wide
Sidewalks

*815 Feet

* approximate linear feet

Existing Stop
Signs to have
stop bar re-
striped



Overhead
Utility Lines

New crosswalk
striping: 13 total
(7): Mid block
(6): Stop Controlled
(with ADA mats)



Progress Photos



GOLDEN GATE • HOBE SOUND • JENSEN BEACH • PALM CITY • PORT SALERNO • RIO



Before



After



Before



After



Sidewalk Numbers

Pre Construction Meeting: February 11, 2020
Final Construction Walkthrough: June 25, 2020

Budget: 158,000

Cost: \$127,483

1,300 Linear Feet of Sidewalk

13 Painted Crosswalks

7 Crosswalk Signs

8 Painted Stop Bars

2 Drainage Crossings Improvements



GOLDEN GATE • HOBE SOUND • JENSEN BEACH • PALM CITY • PORT SALERNO • RIO

